The stopwatch needs two dates.

Torus says Foundry can reach running AI workloads in 12–16 weeks. The public clock is still missing fixed endpoints.

THE DELIVERY CLOCK / FIX BOTH ENDS




12–16 weeks needs one clock.

Customer-level start and accepted-finish dates were unpublished at the cutoff.

> **A fast stage is not yet an auditable whole journey.**

Prefabrication moves work. It does not erase it.

Shorter site work can follow substantial preparation elsewhere and earlier.

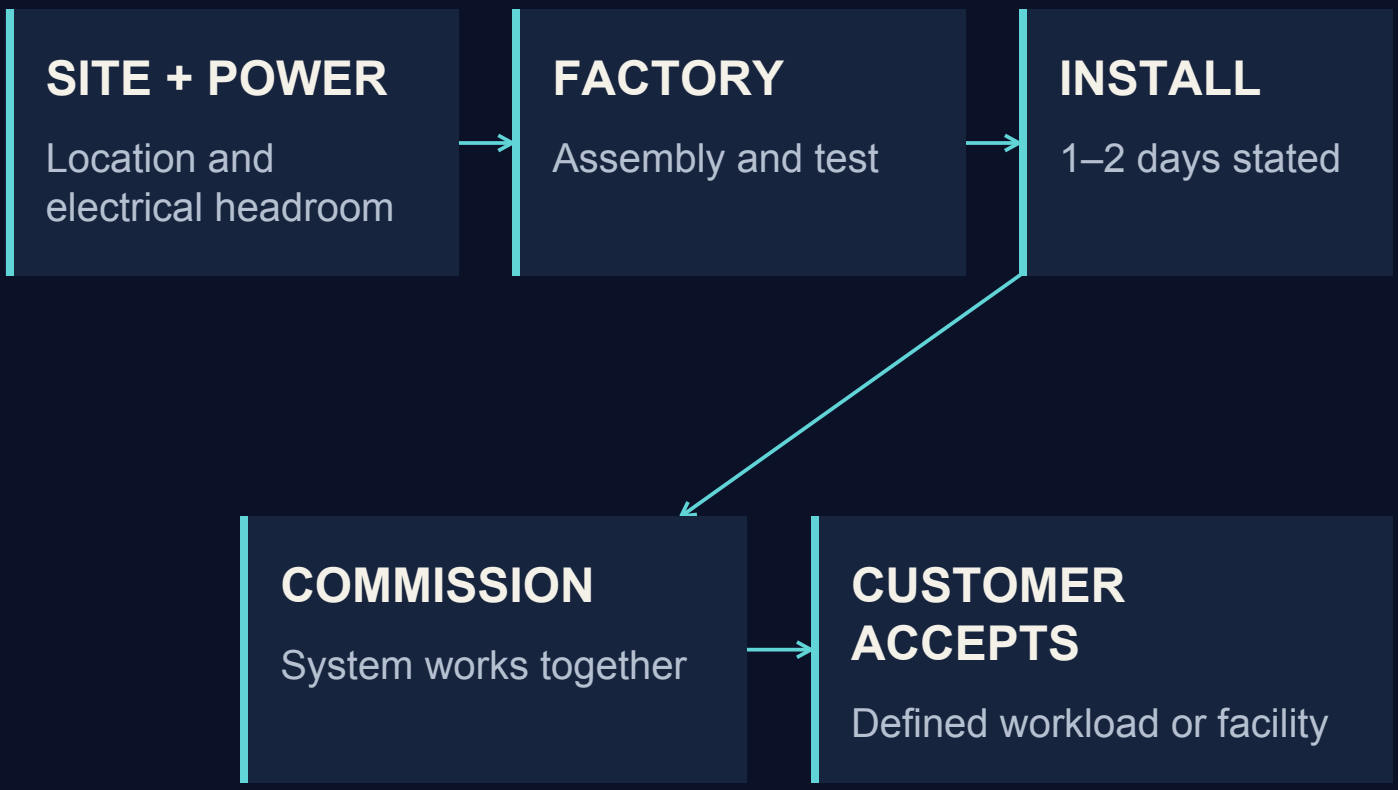

Torus states about one week of site preparation before installation and commissioning.

Measure the whole dependency chain—not only the visible install.

One promise.
Two starting lines.

Contract and site work can be different events with different amounts of preparation before them.

LAUNCH ANNOUNCEMENT

Contract

Commercial milestone

May precede site work

Captures more waiting if used consistently

PRODUCT PAGE

Dirt

Site-work milestone

May follow planning

Can describe a shorter physical stage

Either can be useful. A comparable interval must choose and date one.

The start label determines what the benchmark includes.

“Token” changes with the product.

Three commercial models can place the accepted finish at different points.

MODEL	PUBLISHED OFFER	POSSIBLE FINISH
Strategic	Powered shell; GPUs separate	Facility accepted
Partner	Power, enclosure + GPUs	Workload accepted
Direct	Dedicated inference capacity	Customer workload runs

The exact contractual acceptance event was unpublished for an identifiable customer.

> **Name what the customer bought before naming delivery complete.**

First token is not the final economics.

Technical operation, reliable service and value capture are separate gates.

01
Installed
Equipment is connected and commissioned.

02
First workload
One accepted task runs.

03
Reliable service
Outages and recovery are measured.

04
Utilized capacity
Customer demand keeps equipment busy.

05
Economics
Delivered cost and revenue establish return.

The reviewed sources did not publish customer-level operating results for Foundry.

> **Speed matters—but only alongside reliability, utilization and cost.**

S1 · S2 · S3 · S4 | Operating evidence ladder

The next proof can fit on one receipt.

A small dated record would turn the benchmark into a reproducible interval.

FIELD	WHAT IT FIXES	WHY IT MATTERS
Customer + model	Unit of analysis	Same deployment
Start date	Contract or site work	Starts one clock
Accepted finish	What became usable	Stops that clock
Operating window	Uptime + utilization	Tests economics

Two dates measure delivery. The operating window measures what followed.

> **Bind every field to one customer deployment.**

The build may be fast. Start the public clock.

Foundry's mechanism can compress site work while its customer-level interval remains unverified.

MEMORABLE CLAIM

12–16 weeks

Which two dates stop the same clock?

Name the start. Define acceptance. Then observe operation.

Vendor-stated benchmark · Customer interval unpublished

> **Two dates turn a memorable promise into a measurable delivery record.**
